



ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	4, '18	M	T	W	T	F	S
1			MOBILIZE	1 day	Mon 11/5/18	Mon 11/5/18								
2			CHIP AND REMOVER COAL TAR	5 days	Mon 11/5/18	Fri 11/9/18								
3			STRUCTURAL WORK	30 days	Mon 11/12/18	Fri 12/21/18	2							
4			HOLIDAY WEEK	10 days	Mon 12/24/18	Fri 1/4/19	3							
5			BLAST AND COAT INTERIOR ROOF	25 days	Mon 1/7/19	Fri 2/8/19	4							
6			BLAST AND COAT INTERIOR SHELL	5 days	Mon 2/11/19	Fri 2/15/19	5							
7			BLAST AND COAT INTERIOR FLOOR	5 days	Mon 2/18/19	Fri 2/22/19	6							
8			COAT EXTERIOR UPGRADES	7 days	Mon 2/25/19	Tue 3/5/19	7							
9			CATHODIC INSTALLATION	2 days	Wed 3/6/19	Thu 3/7/19	8							
10			EXTERIOR TOUCH UPS	3 days	Fri 3/8/19	Tue 3/12/19	9							
11			WASH AND DISINFECT	2 days	Wed 3/13/19	Thu 3/14/19	10							


Project: Oak Creek No2 Schedu Date: Mon 11/26/18	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

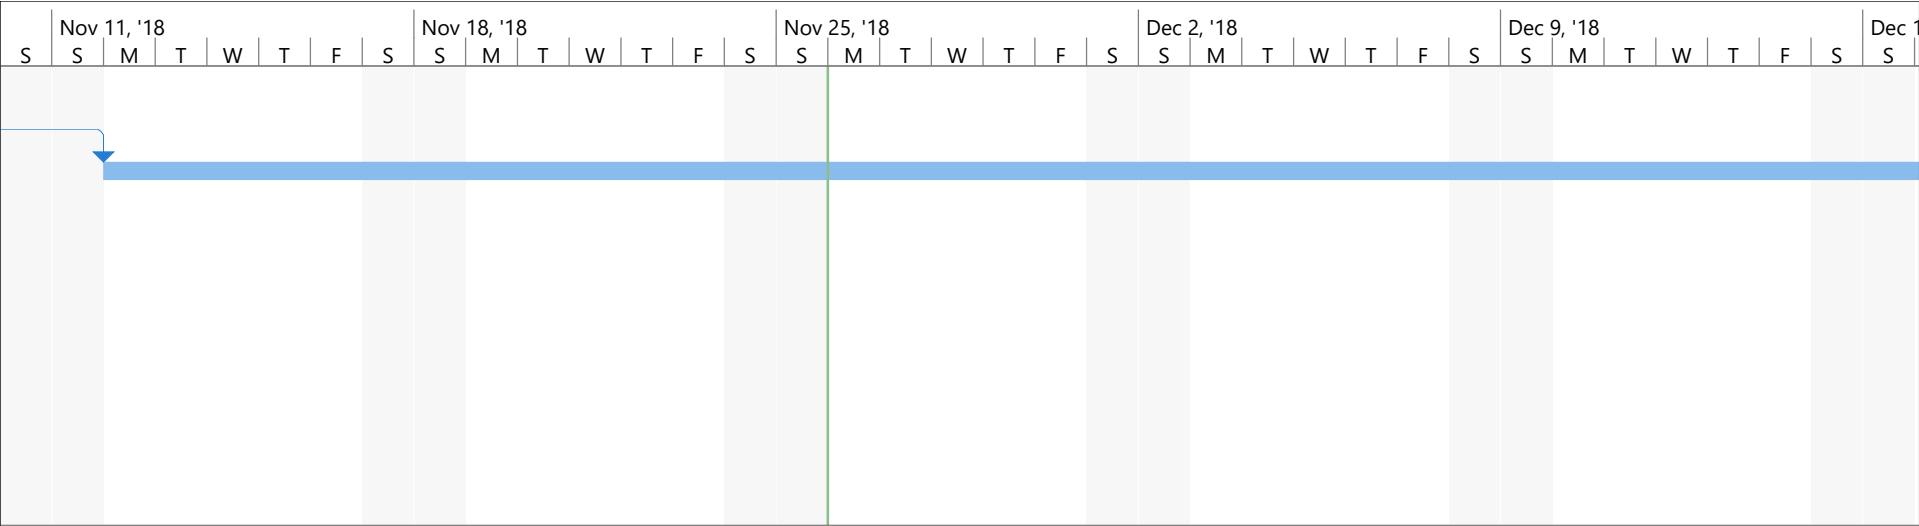

Project: Oak Creek No2 Schedu Date: Mon 11/26/18	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

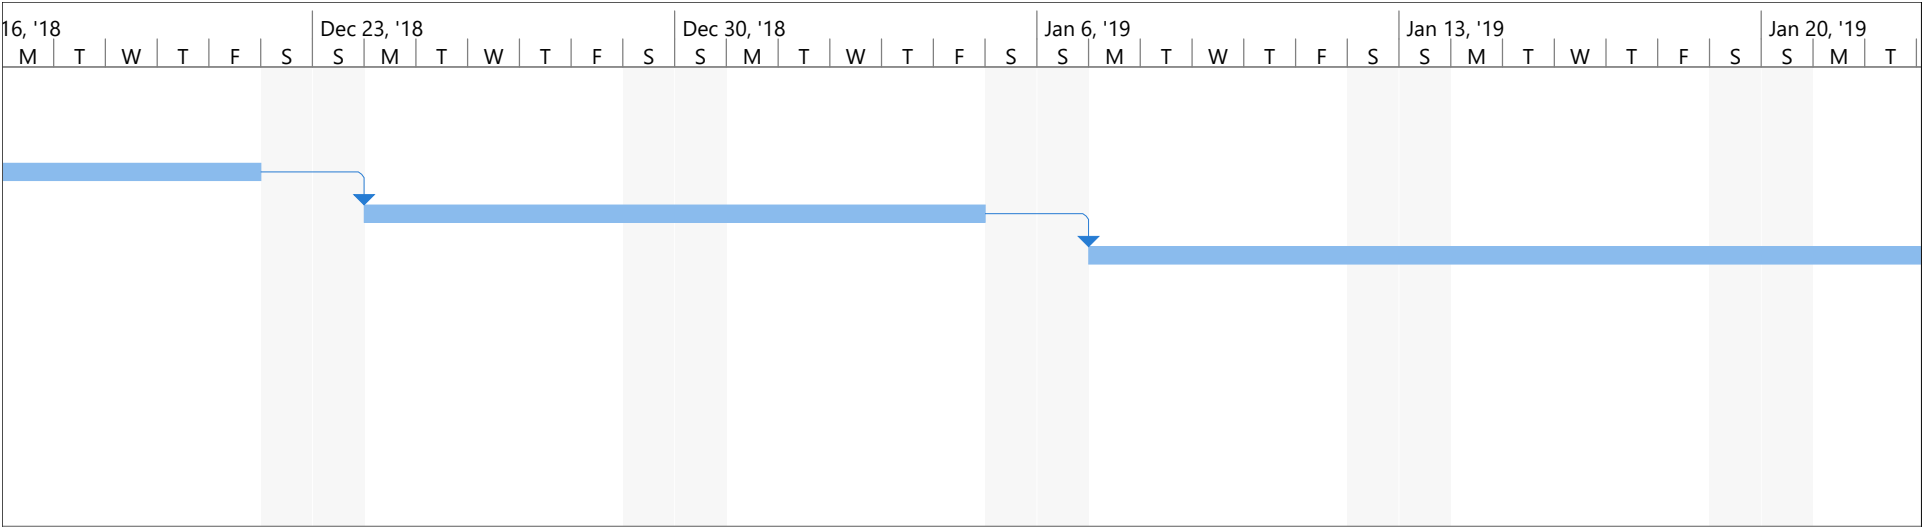

Project: Oak Creek No2 Schedu Date: Mon 11/26/18	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

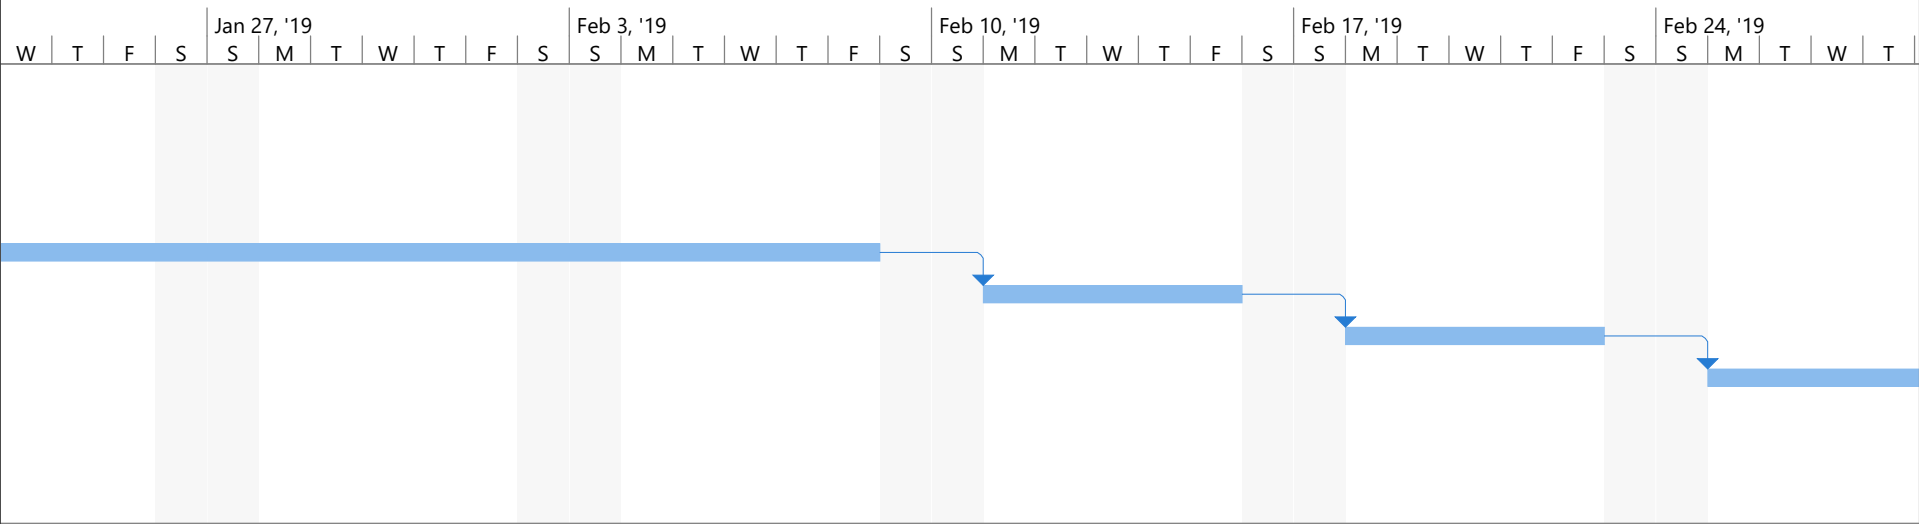

Project: Oak Creek No2 Schedu Date: Mon 11/26/18	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

November 2018

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
				1	2	3
4	5	6	7	8	9	10
	MOBILIZE, 1 day	CHIP AND REMOVER COAL TAR, 5 days				
11	12	13	14	15	16	17
	STRUCTURAL WORK, 30 days					
18	19	20	21	22	23	24
	STRUCTURAL WORK, 30 days					
25	26	27	28	29	30	
	STRUCTURAL WORK, 30 days					

December 2018

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
						1
STRUCTURAL WORK, 30 days						
2	3	4	5	6	7	8
STRUCTURAL WORK, 30 days						
9	10	11	12	13	14	15
STRUCTURAL WORK, 30 days						
16	17	18	19	20	21	22
STRUCTURAL WORK, 30 days						
23	24	25	26	27	28	29
	HOLIDAY WEEK, 10 days					
30	31					
HOLIDAY WEEK, 10 days						

January 2019

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
		1	2	3	4	5
HOLIDAY WEEK, 10 days						
6	7	8	9	10	11	12
	BLAST AND COAT INTERIOR ROOF, 25 days					
13	14	15	16	17	18	19
BLAST AND COAT INTERIOR ROOF, 25 days						
20	21	22	23	24	25	26
BLAST AND COAT INTERIOR ROOF, 25 days						
27	28	29	30	31		
BLAST AND COAT INTERIOR ROOF, 25 days						

February 2019

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
					1	2
BLAST AND COAT INTERIOR ROOF, 25 days						
3	4	5	6	7	8	9
BLAST AND COAT INTERIOR ROOF, 25 days						
10	11	12	13	14	15	16
	BLAST AND COAT INTERIOR SHELL, 5 days					
17	18	19	20	21	22	23
	BLAST AND COAT INTERIOR FLOOR, 5 days					
24	25	26	27	28		
	COAT EXTERIOR UPGRADES, 7 days					

March 2019

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
					1	2
	COAT EXTERIOR UPGRADES, 7 days					
3	4	5	6	7	8	9
COAT EXTERIOR UPGRADES, 7 days			CATHODIC INSTALLATION , 2 days		EXTERIOR TOUCH UPS, 3 days	
10	11	12	13	14	15	16
EXTERIOR TOUCH UPS, 3 days			WASH AND DISINFECT , 2 days			
17	18	19	20	21	22	23
24	25	26	27	28	29	30
31						
